




Design & Construction Schedule

Preconstruction

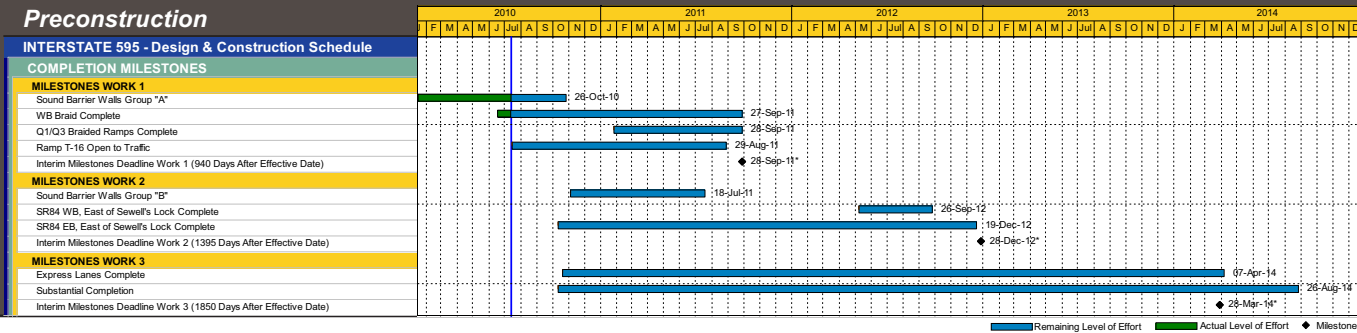

***BASELINE SCHEDULE TO BE APPROVED IN SEPTEMBER 2010**

Item	Milestone	Required Date	Planned Achievement Date
1	Sound Barriers Group A ("Interim Milestone Works 1")	28-Sep-11	26-Oct-10
2	Ramp T-16 opening for traffic to northbound Florida's Turnpike ("Interim Milestone Works 2")	28-Sep-11	29-Aug-11
3	WB Braid including Ramps L-1 and L-2 and westbound SR-84 from Pine Island Road to Nob Hill Road ("Interim Milestone Works 3")	28-Sep-11	27-Sep-11
4	Interim Milestone Q2 - Q3 Braided Ramps	28-Sep-11	28-Sep-11
5	Sound Barriers Group B ("Interim Milestone Works 5")	26-Dec-12	18-Jul-11
6	SR-84 EB from Sewell Lock to the eastern limits of the Project ("Interim Milestone Works 6")	26-Dec-12	19-Dec-12
7	SR-84 WB including complete connections to Ramp T-16, from Sewell Lock to the eastern limits of the Project ("Interim Milestone Works 7")	26-Dec-12	26-Sep-12
8	Express Lanes (I-595) including revenue collection, with or without access to Florida's Turnpike ("Interim Milestone Works 8")	26-Mar-14	7-Apr-14
9	Substantial Completion	26-Mar-14	26-Aug-14
10	Final Acceptance	24-Jun-14	31-Oct-14
